

Daily Operations & Multi-Site Summary

Comprehensive overview of site development, farm operations, residential maintenance, and security status.

GOLF PROJECT

Dam Excavation

Commenced + Green 2
topsoil

DAILY MILK
PRODUCTION

6.0 Litres

Morning: 2.5L | Evening:
3.5L

CHAKA FARMS

Cattle Spraying

Livestock health
maintenance

KABETE RESIDENCE

Sentry Works

Skimming, plumbing &
tank slab



1. Golf Project (Mcheru World of Golf)

Dam excavation commenced, Green No. 2 topsoil removal, and continued site clearance

Overseen by: **Mr. Gichuhi & Ken**



Dam Excavation

- **Dam Excavation Commenced:** Excavation of the dam began at **9:00 AM**, marking the start of a key infrastructure phase for the golf course water management system.
- **Soil Dumping on Tee Boxes:** Excavated soil was transported and strategically dumped on **Tee Box 5, 6, 8, and 9** for grade build-up and terrain shaping.

⚠️ Equipment Breakdown Notice

One of the trucks experienced a mechanical breakdown during operations. The remaining excavation and soil transport work was completed using **a single truck** for the rest of the day.

📺 [Dam Excavation & Soil Dumping Video](#)

📺 [Dumping Excavated Soil](#)



Green No. 2 Earthworks & Site Clearance

- **Green No. 2 Topsoil Stripping:** Stripping of the top layer soil on Green No. 2 was carried out.

- **Stripped Soil Transport:** The stripped topsoil from Green No. 2 was moved and relocated to a designated dump area.
- **Foliage Removal:** Removing foliage from the previously felled trees along the site perimeter.

🌴 Landscaping — Palm Tree Planting

- **Palm Tree Hole Digging:** Started digging holes in preparation for planting palm trees across the golf course landscape.

👔 Executive Site Presence

- **Joe Kamau on Site:** Mr. Joe Kamau was present on site to oversee and review the ongoing golf project operations.

📷 Golf Project Visual Documentation



Dam Excavation

Initial excavation work on the golf course dam.



Dam Excavation — Continued

Active excavation operations on site.



Excavated Soil Dumped on Tee Boxes

Soil dumped on Tee Box 5, 6, 8 & 9.



Lorry Dumping Dam Soil

Transport truck dumping excavated dam soil.



Excavated Soil Transport

Lorry dumping excavated soil at tee box zone.



Topsoil Stripping — Green No. 2

Stripping the top layer soil on Green 2.



Green No. 2 — Stripped

Top layer soil fully stripped on Green 2.



Stripping & Moving Soil — Green No. 2

Stripping and relocating topsoil from Green 2.



Moving Stripped Topsoil

Transporting stripped soil from Green 2.



Foliage Removal

Removing foliage from felled trees.



Joe Kamau — On Site

Mr. Joe Kamau present for project review.



Digging Holes for Palm Trees

Excavating planting holes for palm trees.



Palm Tree Planting Hole
Prepared hole ready for palm tree planting.



2. Farm Activities & Upkeep (Chaka Farms)

Cattle spraying, dairy production, and canine training



Livestock Management & Dairy

Overseen by: **Kamandau**

- **Cattle Spraying:** All cattle were sprayed for tick and pest control as part of routine livestock health maintenance.

SESSION	MORNING	EVENING	TOTAL
Milk Yield	2.5 Litres	3.5 Litres	6.0 Litres



Cattle Spraying
Tick and pest control spraying on cattle.



Canine Unit — Care & Training

Overseen by: **Willy**

- **Kennel Sanitation:** Kennels were thoroughly cleaned and fresh water was provided to all dogs.
- **Kennel Manners:** Kennel discipline and etiquette drills were conducted.
- **Walking Off-Leash:** All dogs participated in off-leash walking exercises.

- **Kennel Swap — Coby & Logan:** Coby and Logan were switched to different kennels to reduce noise at night.
- **Full Commands Training:** All command training drills were conducted today including **Sit**, **Paw**, **Down**, as well as **patience and obedience** exercises.

📺 Canine Training Videos

🎬 [Walking Off-Leash](#)

🎬 [All Commands Training.\(Part 1\)](#)

🎬 [All Commands Training.\(Part 2\)](#)

📁 Dogs Album (Google Drive Folder)

📁 [View Full Dogs Album on Google Drive](#)

📷 Dog Album — Daily Snapshots



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Canine Unit



Coby & Logan — Kennel Swap

Switched kennels to reduce nighttime noise.



Security Status (Chaka Farms — Near Brookside / Honi)



Status: No New Activity

No new activity on Chaka Farms near Brookside (Honi). Standard perimeter monitoring maintained — no incidents to report.



3. Facility Maintenance (Kabete Residence)

Sentry finishing works, plumbing, roof tiles, tank slab demolition, and office furnishing



Sentry Construction & Finishing Works

- **Sentry Skimming:** Wall skimming and plaster finishing applied to the sentry structure.
- **Sentry Bathroom Skimming:** Interior skimming completed on the sentry bathroom walls.
- **Guard Handwash Tap Installation:** A new handwash tap was installed for the guards at the sentry point.
- **Sentry Handwash Fitting:** Plumbing and fixture fitting completed for the sentry handwash station.



Roofing, Painting & Tank Works

- **Roof Tile Fitting (Hanging Lines Area):** Roof tiles were fitted and secured near the hanging lines section of the main house.
- **Fascia Boards Painting:** Painting of the fascia boards near the hanging lines was completed.
- **Main House Water Tank Slab Demolition:** Demolishing of the concrete slab for the main house water tank structure to prepare for rebuilding.

Office & Interior Furnishing

- **Wall Pictures Installation:** Decorative wall pictures were installed in the office.
- **Bookshelf Organization:** Books were placed back on the shelf after the wall picture installation and office rearrangement.

Kabete Residence Visual Documentation




Sentry Skimming

Wall skimming on the sentry structure.




Sentry Bathroom Skimming

Interior plaster finishing on sentry bathroom.

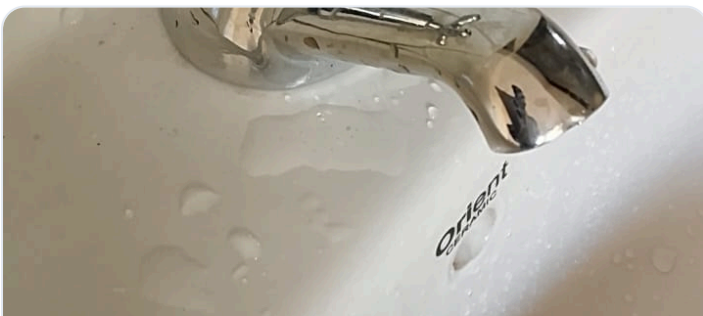

Guard Handwash Tap

New handwash tap installed for guards.

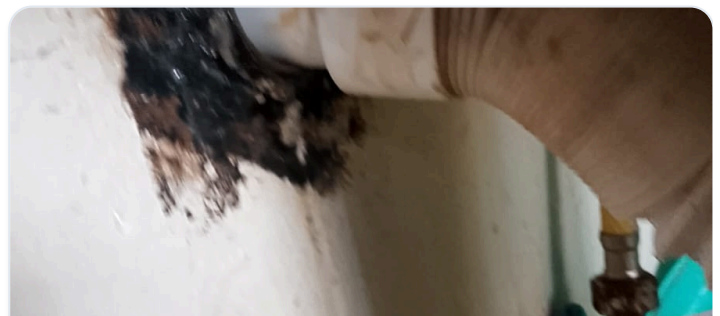

Sentry Handwash Fitting

Plumbing fitting for sentry handwash station.



Roof Tile Fitting

Fitting roof tiles near the hanging lines.



Fascia Boards Painting

Painting fascia boards near the hanging lines.



Water Tank Slab Demolition

Demolishing the main house water tank slab.



Tank Slab Demolition — Continued

Continued demolition of the tank concrete slab.



Main House Tank Foundation

New foundation being prepared for the water tank.




Foundation Sand

Sand extracted from the tank foundation works.



Main House Roof Painting

Continued paintjob on the main house roof.

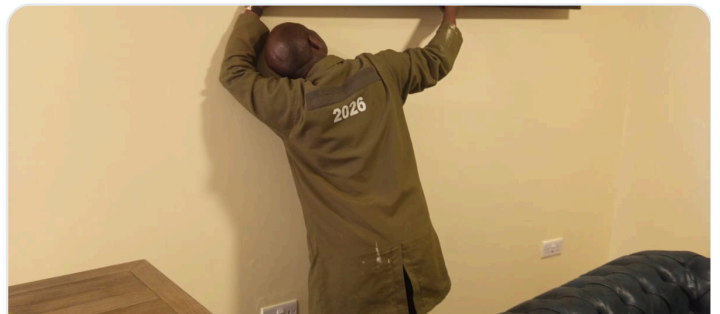

Office Wall Pictures

Decorative wall pictures installed in the office.



Bookshelf Organization

Books placed back on the shelf after rearrangement.



Office Radio Stand

Radio stand set up in the office.



Main House Storage Box

New storage box for the main house.



Io & Rio — Dinner Time

The cats enjoying their evening meal at Kabete Residence.

DN

Compiled by Dennis Ndirangu
