DAILY OPERATIONS REPORT

Friday, 9th October 2026

Daily Operations Progress Report

Comprehensive engineering, agronomy, livestock production, civil construction, and estate management across all active project sites.

COURSE DRAINAGE & AGRONOMY

Greens 5, 8 & 14

PVC Outlet Drainage Connected

RIVERSAND LAYER SPREADING

Greens 7 & 16

Sand Over Pumice Bed Advanced

GROSS DAIRY PRODUCTION

6.0 Litres

5.0L Sold • 1.0L Staff (100% Reconciled)

DAM & ESTATE INFRASTRUCTURE

Dam 2 Inlet Pipe

Installed • Inflows into Dams 1, 2 & 3

Executive Summary & Multi-Site Operational Synthesis

Field operations on Friday, 9th October 2026 registered substantial engineering, agronomic, livestock, and civil construction accomplishments across all four active sites. At Mucheru World of Golf, trenching teams measured trench parameters in the morning and excavated dual-purpose inlet and drainage trenches connecting greens and teeboxes. Long runs of orange PVC piping were connected to the outlet drainage systems for Greens 5, 8, and 14, supported by the farm tractor hauling pipe shipments from the greenhouse. Riversand spreading commenced on Green 7 but was paused due to heavy murram mud on the access perimeter, with operations pivoting to Green 16 where sand was mostly applied over the pumice bed. On the water infrastructure front, the Dam 2 water inlet pipe was installed and is ready to receive water, while inlet pipelines feeding Dam 1 and Dam 3 maintained steady replenishment. At Chaka Farms, dairy milking achieved 6.0 Litres gross harvest with 100% volume reconciliation (5.0L commercial sales, 1.0L internal staff rations). Willy oversaw canine unit kennel manners, cleaning, paw command drills, and farm off-leash walking. Ken mobilized an electric pump to drain accumulated floodwater from the farm island into the dam and supervised Barleria hedge planting at Gate A, while Margaret and Monica planted manured maize seeds. At Kabete Residence, masons and carpenters offloaded timber, cut marine board, fitted and erected column formwork for the SQ outdoor fireplace, and water-cured the river forest retaining wall, alongside domestic pet care. At Amani Cottage, Edwin swept grounds, collected litter, planted yucca plants, and recorded 0.3 m³ water consumption.

- **Mucheru World of Golf:** Field crew measured trench parameters (width, depth) in the morning and dug network trenches for water inlet and drainage to and from greens and teeboxes; orange PVC drainage pipes were connected to Greens 5, 8, and 14 outlet trenches; the farm tractor hauled trailer loads of PVC pipes from the greenhouse; riversand was applied partially on Green 7 (suspended due to muddy murram surrounds) and moved to Green 16 where sand was mostly applied over the pumice bed; Dam 2 water inlet pipe was installed ready for water inflow; and Dam 1 and Dam 3 water inlet lines continued active progress.
- **Chaka Farms:** Dairy production achieved 100% mathematical reconciliation at 6.0 Litres gross (3.5L morning, 2.5L evening; 5.0L total commercial sales, 1.0L internal staff rations for Gladys and Maasai; goat kids fully weaned); Willy supervised kennel manners, stall sanitation, paw command, and afternoon off-leash walking; Ken operated an electric powered pump to remove floodwater from the farm island into the dam and planted Barleria hedge plants at Gate A; Margaret and Monica worked with Kimondo digging holes, applying manure, and planting maize seeds.
- **Kabete Residence:** Construction crew offloaded a pick-up delivery of timber; carpenters cut marine board sheets for formwork shutters; column formwork was fitted and installed for concrete casting at the SQ outdoor fireplace; masonry workers conducted water curing on the retaining wall and columns in the river forest area; domestic pet care routines were maintained for Ajabu and resident cats (Reo, Mocha, and Aiko). Operational oversight and updates shared by Njoki.
- **Amani Cottage:** Edwin swept entrance driveways, stepping stone paths, and garden lawns, collecting fallen litter; planted yucca plants along garden borders; and logged 0.3 m³ water consumption for daily estate upkeep.

🌟 Key Operational Milestones Achieved Today

PVC outlet drainage pipes connected to Greens 5, 8, and 14; riversand mostly spread across Green 16 pumice layer; Dam 2 water inlet pipeline installed and operational; Chaka Farms dairy achieved 100% reconciliation at 6.0L; farm island rainwater flooding successfully pumped out into the dam; Barleria perimeter hedge planting advanced at Gate A; and structural column formwork erected at the Kabete SQ fireplace.

Mucheru World of Golf

Overseen by: Mr. Gichuhi & Ken

⛳ Green Drainage PVC Connected, Trench Excavation, Riversand Spreading & Dam 2 Inlet Installed

Operations on Friday, 9th October 2026 registered extensive advancements across drainage hydraulics, precision agronomy, earthwork trenching, and dam infrastructure:

> ### Mucheru World of Golf Operations Summary
>
> Trench parameters were measured and excavation advanced for inlet and drainage lines serving greens and teeboxes; PVC pipes were connected to outlet drainage trenches for Greens 5, 8, and 14; the farm tractor hauled PVC pipe loads from the greenhouse; riversand was partially applied to Green 7 before muddy surrounds prompted a shift to Green 16 where sand was mostly applied; Dam 2 water inlet pipe was installed; and Dams 1 and 3 continued receiving water inflows.

- **Trench Parameter Measurement & Excavation:** In the morning, site supervisors and surveying crew measured trench dimensions (width, depth, and fall gradients) across the course. Manual crews with picks and shovels actively dug trenches designed for stormwater runoff drainage and incoming sprinkler irrigation lines serving putting greens and championship teeboxes.
- **PVC Outlet Drainage Connected to Greens 5, 8 & 14:** Long lines of heavy-duty orange PVC piping were laid and connected directly into the excavated outlet drainage trenches for Green 5, Green 8, and Green 14. These pipeline runs ensure positive gravity discharge of excess subsurface water from green basins to prevent waterlogging during rains.
- **PVC Pipe Haulage by Farm Tractor:** The farm tractor and red trailer were mobilized to transport bundles of orange PVC pipes from greenhouse storage across the property to active trenching corridors on the golf course.
- **Riversand Spreading on Greens 7 & 16:** Sand application commenced over the pumice layer on Green 7; however, surrounding red murram access tracks became too muddy for wheelbarrow passage, leading the crew to pause Green 7 after partial sand placement. The team shifted to Green 16, where wheelbarrow teams pushed sand across the pumice profile, completing the majority of the green area.
- **Dam 2 Water Inlet Pipeline Installed:** The dedicated black HDPE water inlet pipeline feeding Dam 2 was laid in its supply trench and fully connected. With installation complete, Dam 2 is ready to receive water inflows.
- **Dams 1 & 3 Continuous Water Inflow:** Pipeline inlets discharging into Dam 1 and Dam 3 continued active flow, steadily replenishing the course's irrigation storage reservoirs.

🎬 Video Documentation — Mucheru World of Golf Daily Operations

📹 VIDEO RECORDING

Comprehensive video field documentation capturing Friday's operations at Mucheru World of Golf: morning trench parameter measurements, excavation of inlet and drainage trenches for greens and teeboxes, laying and connecting orange PVC pipes to Greens 5, 8, and 14 outlet trenches, tractor pipe haulage, partial riversand spreading on Green 7, major riversand coverage on Green 16, installation of Dam 2 water inlet pipe, and ongoing inflow into Dams 1 and 3.

▶ Watch on YouTube

URL: https://youtu.be/wwkF_SP0HOY

⛳ Course Agronomy & Engineering Status Audit — Putting Greens (1 – 18)

Audited by: Dennis

18-hole putting green status audit showing the latest work completed and current condition for each green as of October 9, 2026:

GREEN	CURRENT TECHNICAL & AGRONOMIC STATE	MILESTONE STATUS
Green 1	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 2	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 3	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 4	Outlet drainage trench excavated across fairway corridor to safely discharge runoff (Oct 5).	Outlet Drainage Dug
Green 5 TODAY	Connected PVC pipes to green outlet drainage trench for excess runoff and sprinkler lines (Oct 9).	Drainage PVC Connected
Green 6	Surplus red soil applied to raise and level surrounds (Sep 28).	Apron Raised • Palms Placed
Green 7 TODAY	Riversand partially applied over pumice bed; paused as surrounding murram soil was too muddy (Oct 9).	Riversand in Progress
Green 8 TODAY	Connected PVC pipes to outlet drainage trench to convey excess runoff and house supply lines (Oct 9).	Drainage PVC Connected
Green 9	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 10	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 11	Riversand application in progress over pumice bed; partial coverage completed (Oct 3).	Riversand in Progress
Green 12	Surplus red soil (from 1 truck delivery) applied and leveled around collar and surrounds (Oct 2).	Surplus Red Soil Applied
Green 13	Surplus red soil spread around surrounds to raise and match green level (Sep 29).	Surplus Red Soil Applied
Green 14 TODAY	Connected PVC pipes to green outlet drainage trench to remove surplus stormwater (Oct 9).	Drainage PVC Connected
Green 15	Riversand applied over pumice bed across most part of green (Oct 3).	Riversand Applied (Most Part)
Green 16 TODAY	Riversand applied over pumice bed across most part of green; application ongoing to completion (Oct 9).	Riversand in Progress
Green 17	Surplus red soil spread around surrounds to raise and align levels (Sep 29).	Surplus Red Soil Applied
Green 18	Surplus red soil spread and leveled around collar and surrounds (Sep 30).	Surplus Red Soil Applied

🏌️ Course Engineering Status Audit — Championship Teeboxes (1 – 18)

Audited by: Dennis

Comprehensive 18-hole championship teebox platform audit tracking earthwork leveling, structural embankments, and playing corridor alignments as of October 9, 2026:

TEEBOX	CURRENT TECHNICAL & EARTHWORK STATE	PLATFORM STATUS
Tee 1	Championship launch platform completely reshaped, cut, and graded to design elevation using Backhoe Loader (Sep 24); received 1 lorry red soil delivery (Sep 26).	Platform Reshaped
Tee 2	Playing launch platform completely reshaped, contoured, and graded using Backhoe Loader (Sep 24); received 1 lorry red soil delivery (Sep 26).	Platform Reshaped
Tee 3	Playing launch platform completely reshaped, contoured, and graded using Backhoe Loader (Sep 24); received 1 lorry red soil delivery (Sep 26).	Platform Reshaped
Tee 4	Championship launch platform completely reshaped, cut, and graded using Backhoe Loader (Sep 23); received 1 lorry red soil delivery (Sep 26).	Platform Reshaped
Tee 5	Main perimeter drainage pipeline backfilled all the way past Maina's place (Oct 2).	Drainage Backfilled
Tee 6	Precision leveling and compaction completed; fresh delivery of 1 lorry red loam topsoil unloaded at platform surrounds (Sep 26).	Red Soil In • Leveled
Tee 7	Both number 7 teebox platforms actively reshaped, cut, and leveled by crew under Joe Kamau and supervisors (Oct 4).	Both Platforms Reshaped
Tee 8	Graded, leveled, and contour-adjusted; fresh delivery of 1 lorry red loam topsoil unloaded directly on platform (Sep 26).	Red Soil In • Graded
Tee 9	Playing platform leveled and surrounding perimeter ground graded (Sep 1); received 1 lorry red soil delivery (Sep 26).	Platform Leveled
Tee 10	Graded and compacted platform serving the start of the back-nine playing corridor; received 1 lorry red soil delivery (Sep 26).	Platform Compacted
Tee 11	Playing launch platform actively shaped, graded, and refined to final architectural contours and levels (Oct 8).	Shaped & Refined
Tee 12	Both championship and forward platforms actively shaped, leveled, and refined to finished design elevation (Oct 8).	Shaped & Refined
Tee 13	Playing platform earthworks completely finished, shaped, and refined to final design elevation and contours (Oct 7).	Finished & Refined
Tee 14	Launch platform earthworks completely finished, shaped, and refined to final playing contour (Oct 7).	Finished & Refined
Tee 15	Launch platform shaping completely finished; terrace cut to design elevation and precision leveled (Oct 6).	Platform Reshaped
Tee 16	Surplus red soil moved onto platform; launch terrace completely reshaped and leveled (Oct 5).	Platform Reshaped
Tee 17	Launch platform reshaped, cleared of brush, and graded to playing corridor alignment (Oct 6).	Platform Reshaped
Tee 18	Championship tee platform leveled; perimeter approach cleared and graded (Sep 1); received 1 lorry red soil delivery (Sep 26).	Platform Leveled

Operations Agronomy & Engineering Synthesis

Putting Greens & Hydraulic Progress: Orange PVC drainage pipes connected to outlet trenches on Greens 5, 8, and 14; trench parameters measured and network trenching underway for greens and teeboxes; riversand partially placed on Green 7 and mostly applied on Green 16; all 18 greens (100%) have subgrade foundations excavated and membrane lined; 100% have volcanic pumice layers compacted; Dam 2 water inlet pipe installed; active water replenishment continuing for Dams 1, 2, and 3.
Championship Teebox Platforms: Teeboxes 11, 12, 13, and 14 completely shaped, graded, and refined; drainage and water inlet trenches excavated connecting teebox and green zones; course playing corridors primed for grass planting.

📸 Photographic Field Evidence — Mucheru World of Golf

Sequential photographic field documentation covering trench parameter measurement, drainage trench excavation, PVC pipe hauling and connection (Greens 5, 8 & 14), riversand spreading (Greens 7 & 16), and dam water inlet installations (Dams 1, 2 & 3):

Measuring Trench Parameters Across Course

Crew using tape measure to check trench width, depth, and fall alignment between greens and tees in the morning.

Manual Drainage Trench Excavation

Workers using picks and shovels to dig network trenches for green and teebox drainage and water supply.

Green 4 Fairway Trench Line

Aerial drone capture showing the extended drainage trench line running from Green 4 across the fairway corridor.

Green 8 Drainage Trench Route

High-altitude aerial view of Green 8 showing the drainage trench excavated across the subgrade profile towards the perimeter.

Green 8 Trenching Corridor Overview

Drone perspective showing the trench excavation alignment and pipe placement extending out from Green 8.

Farm Tractor Hauling PVC Pipes

Tractor and red trailer transporting a full load of orange PVC pipes from greenhouse storage to the golf site.

PVC Drainage Pipes Staged on Site

Stockpile of heavy-duty PVC drainage pipes delivered and staged along the green construction corridors.

PVC Pipe Jointing & Alignment

Plumbing crew jointing and assembling lengths of orange PVC pipes along the excavated trench line.

Laying PVC Pipe in Green 5 Trench

Orange PVC drainage pipe laid directly inside the deep drainage trench extending from Green 5.

Fitting PVC Outlet Pipe for Green 5

Workers aligning pipe gradients to ensure proper gravity fall for Green 5 stormwater runoff.

Green 5 PVC Pipeline Connection Aerial

Drone capture showing the continuous orange PVC pipeline laid in the trench beside Green 5 with laborers connecting sections.

Hauling Riversand Over Muddy Murram at Green 7

Worker pushing a wheelbarrow of riversand along wooden planks over wet, muddy murram surrounds at Green 7.

Green 7 Partial Riversand Coverage Aerial

Aerial drone view of Green 7 showing the upper portion covered in riversand before work was suspended due to muddy surrounds.

Green 7 Pumice Profile & Sand Pile

Ground view of the contoured pumice bed of Green 7 with large stockpiles of coarse riversand adjacent.

Green 7 Agronomic Subgrade View

Close-up perspective of the leveled pumice foundation and surrounding red soil shaping on Green 7.

Wheeling Riversand onto Green 16

Laborer wheeling riversand directly onto Green 16 after operations shifted from Green 7.

Spreading Sand Across Green 16 Pumice Bed

Crew manually distributing and raking riversand over the underlying compacted pumice foundation of Green 16.

Green 16 Riversand Mostly Applied Aerial

Drone capture of Green 16 showing roughly 80% riversand coverage across the green with the wheelbarrow team actively working.

Advanced Riversand Layer on Green 16

Ground-level progress view of Green 16 showing advanced sand coverage ready for leveling and final grading.

Dam 2 Water Inlet Pipeline Laid in Trench

Newly installed black HDPE inlet water pipe running through an excavated trench directly into the Dam 2 reservoir basin.

Dam 2 Reservoir & Water Inlet Overview

Dam 2 lined reservoir showing anchored perimeter polythene and the newly connected inlet supply pipeline.

Dam 2 Basin Aerial Perspective

Drone aerial capture of the Dam 2 basin with liner secured in anchor trenches, prepared to receive incoming water.

Dam 1 Water Inflow Progress Aerial

Aerial overview of Dam 1 reservoir showing steady inflow and rising water storage reserves.

Dam 3 Inflow Progress Drone Capture

Aerial overview of Dam 3 reservoir showing continuous water inflow through the supply pipeline.

Dam 3 Water Inlet Pipeline Flow

Ground perspective of the water inlet pipe actively discharging fresh water into the Dam 3 storage basin.

Dam 3 Reservoir Basin Overview

Wide drone angle of Dam 3 showing the water accumulation basin and surrounding course terrain.

Chaka Farms

Dairy: Kamandau | Canine Supervisor: Willy | Gardens & Maize: Margaret & Monica | Dewatering & Hedges: Ken

Reconciled Dairy Milking (6.0L Gross), Canine Unit Training, Island Dewatering & Gate Landscaping

Operations at Chaka Farms on Friday, 9th October 2026 registered major accomplishments across dairy production, canine behavioral conditioning, estate hydraulic management, and farm agronomy:

> ### Chaka Farms Operations Summary
>
> Dairy milking yielded 6.0 Litres gross with 100% mathematical reconciliation (5.0L commercial sales, 1.0L internal staff allocations; goat kids fully weaned); Willy supervised kennel manners, stall cleaning, paw command, and off-leash farm exercise; Ken operated an electric powered pump to clear floodwater from the farm island into the dam and supervised planting of Barleria hedge plants at Gate A; and Margaret and Monica worked with Kimondo digging planting holes, applying manure, and planting maize seeds.

- **Reconciled Dairy Production (Kamandau):** Morning milking yielded 3.5 Litres and evening milking yielded 2.5 Litres, totaling 6.0 Litres gross harvest. Commercial sales dispatches stood at 2.5L morning and 2.5L evening (5.0L daily total sold). Routine internal farm disbursements accounted for 1.0L (0.5L Gladys staff ration + 0.5L Maasai security ration), resulting in 100% accounting fidelity with zero discrepancy. Goat kids remain officially weaned (0.0L allocation).
- **Canine Behavioral Conditioning & Off-Leash Walking (Willy):** Willy conducted structured training sessions with the Canine Unit. Routines covered kennel manners (reinforcing patience and boundary respect at open stall doors), thorough stall sanitation, paw command practice, and guided off-leash walking exercise across farm fields to promote physical conditioning and responsiveness.
- **Farm Island Flood Dewatering via Electric Pump (Ken):** Heavy rainwater accumulation that had flooded the central farm island lawn around the trees and seating area was pumped out. Ken and his team set up a mobile electric-powered water pump mounted on a wheelbarrow chassis with a floating suction intake, actively pumping the floodwaters through discharge piping straight into the dam basin.
- **Barleria Hedge Planting at Gate A (Ken):** Ground preparation along Gate A was completed, and the team planted healthy Barleria flower hedge seedlings along the inner perimeter fence line to establish a vibrant, dense security border.
- **Field Maize Planting & Manure Application (Margaret & Monica):** Margaret and Monica performed general compound maintenance and advanced field agriculture. Working alongside Kimondo (who dug planting holes with a jembe), the ladies applied organic farmyard manure into each hole and planted maize seeds across the prepared plot.

📊 Dairy Milking Yield & Utilization Ledger

Milking Supervisor: Kamandau

Quantitative reconciliation of gross dairy harvest, commercial sales dispatches, and internal farm allocations for Friday, 9th October 2026:

Production & Allocation Category	Morning Session	Evening Session	Daily Total	Accounting Classification
Commercial Milk Sales (Dispatched)	2.5 L	2.5 L	**5.0 L**	Commercial Sales Outflow
Goat Kids Milk Ration	0.0 L	—	**0.0 L**	Weaned (Fully Grown & Independent)
Gladys Allocation (Staff)	0.5 L	—	**0.5 L**	Internal Farm Allocation (Staff)
Maasai Allocation (Security)	0.5 L	—	**0.5 L**	Internal Farm Allocation (Security)
Total Internal Farm Allocations			**1.0 L**	**Total Internal Outflow**
Total Gross Cow Milk Harvested (Sales + Allocations)			**6.0 L**	**100% Accounted Production (3.5L AM / 2.5L PM)**

📌 Ground Truth Accounting Note

In accordance with the estate milk reconciliation standard established on October 1st, Kamandau's recorded dispatches of 2.5L morning and 2.5L evening represent commercial milk sold (5.0L total). Internal disbursements comprise 0.5L morning staff ration for Gladys and 0.5L morning security ration for Maasai (1.0L total internal allocations). The goat kids are fully weaned and graze independently (0.0L allocation). Total gross cow milk harvested is exactly 6.0 Litres (3.5L morning harvest [2.5L sold + 1.0L internal allocations] and 2.5L evening harvest [2.5L sold]) with 100% accounting fidelity and zero discrepancy.

🐕 Canine Unit Care, Farm Island Dewatering & Video Documentation

Canine Supervisor: Willy | Dewatering & Grounds: Ken

Daily behavioral training, kennel hygiene, off-leash farm exercise, and hydraulic island dewatering operations conducted on Friday, 9th October 2026:

- **Kennel Manners & Boundary Conditioning (Willy):** Working dogs practiced patience, remaining seated calmly inside open stall gates until given release cues, establishing sound boundary respect and handler attentiveness.
- **Kennel Hygiene & Paw Command Drills:** Complete washing and disinfection of indoor kennels were completed; dogs practiced the paw command calmly.
- **Afternoon Off-Leash Farm Exercise:** Dogs were guided on an energetic off-leash walk across open farm paddocks to encourage social manners, recall, and physical conditioning.
- **Electric Pump Island Dewatering (Ken):** Electric-powered water pump was deployed to eliminate standing rainwater floodwaters covering the central farm island lawn, discharging the water directly into the adjacent dam.

Kennel Manners Drill

🎥 VIDEO RECORDING

Willy conducting kennel manners, boundary control, and structured gate restraint drills with the Canine Unit, reinforcing calm demeanor and attentiveness.

📁 Access on Google Drive

`Kennel manners.mp4 (8.8 MB)`

Island Flood Dewatering

🎥 VIDEO RECORDING

Ken operating the mobile electric-powered pump with floating suction to remove standing rainwater floodwaters from the island lawn and discharge them into the dam.

📁 Access on Google Drive

`Pumping flooded water.mp4 (2.9 MB)`

📸 Photographic Field Evidence — Chaka Farms

Sequential photographic field documentation covering island floodwater removal, Barleria hedge planting at Gate A, and maize planting with manure application:



Rainwater Flooding on Farm Island Lawn

Rainwater pooling across the farm island lawn, submerging the grass around acacia trees and outdoor furniture.

Flooded Lawn & Island Canopy

Broad view of standing water across the island recreation area prior to the deployment of the electric pump.

Setting Up Electric Dewatering Pump

Field crew positioning the mobile electric water pump on the wheelbarrow chassis and connecting the discharge pipe.

Barleria Seedlings Staged at Gate A

Healthy Barleria nursery seedlings in black potting sleeves arranged along Gate A ready for planting.

Planting Barleria Hedge Along Fence

Workers digging a continuous planting trench and setting Barleria seedlings along the inner fence at Gate A.

Close-Up of Barleria Plant Installation

Close-up view of freshly set Barleria plants bedded into enriched red loam soil to form a dense boundary hedge.

Maize Planting & Manure Application in Farm Field

Kimondo digging planting holes with a jembe while Margaret and Monica apply organic farmyard manure and plant maize seeds.

🏡 Timber Offloading, SQ Fireplace Column Formwork, Marine Board Cutting & River Wall Curing

Field operations at Kabete Residence on Friday, 9th October 2026 focused on civil structural carpentry, column formwork installation at the SQ outdoor fireplace, hydraulic water curing along the forest river retaining wall, and domestic pet welfare. Operational oversight and updates were shared by Njoki:

> **Kabete Residence Progress Summary**
>
> Construction crew offloaded a delivery of timber; carpenters cut marine board sheets for formwork; column formwork was fabricated, fitted, and installed at the SQ outdoor fireplace; masonry workers conducted water curing on the retaining wall in the forest river area; and pet care was provided for Ajabu and resident cats.

- **Timber Delivery Offloading:** A fresh consignment of structural building timber was delivered on site via pick-up truck. Laborers offloaded and neatly stacked timber planks and studs near the carpentry workstation for immediate shuttering use.
- **Marine Board Cutting for Formwork:** Carpenters measured and accurately cut marine board sheets and timber battens to fabricate formwork casings for structural reinforced concrete columns.
- **SQ Fireplace Column Formwork Fitting & Installation:** Masons and carpenters actively fitted and erected timber column formwork casings at the SQ outdoor fireplace. Formwork boxes were aligned plumb against the stone masonry, secured with horizontal cross-battens, and firmly braced with timber props in preparation for concrete casting.
- **Retaining Wall Water Curing in River Forest Area:** Thorough water curing was carried out along the heavy-duty stone masonry retaining wall and reinforced concrete column structures in the forest section bordering the river. The wall surfaces and weep hole zones were kept saturated to ensure complete cement hydration and structural strength.
- **Domestic Pet Welfare (Ajabu & Resident Cats):** Complete pet care routines were maintained for Kabete's domestic pets. Ajabu the Golden Retriever enjoyed outdoor exercise and relaxed comfortably on the lawn. Resident cats (Reo, Mocha, and Aiko) were fed together indoors and remained in excellent health.

📸 Photographic Field Evidence — Kabete Residence

Sequential photographic field documentation covering timber offloading, marine board cutting, SQ fireplace column formwork fabrication and installation, river forest retaining wall curing, and domestic pets:

Offloading Timber Delivery from Pick-Up Truck

Workers offloading bundles of structural timber planks from the pick-up truck at Kabete Residence.

Stacking Timber Planks on Site

Planks stacked neatly near the workshop area ready for column formwork fabrication.

Timber Cargo Unloading Progress

Laborers completing offloading of construction timber for the SQ fireplace and structural works.

Cutting Marine Board Sheets

Carpenter accurately cutting marine plywood sheets to build smooth formwork panels for concrete columns.

Formwork Panel Fabrication for SQ Columns

Assembled timber formwork shutter panels with reinforcing cleats prepared for erection at the SQ outdoor fireplace.

Positioning Column Formwork at SQ Fireplace

Carpenters fitting and aligning column shutter boxes against the stone masonry wall at the SQ fireplace.

Vertical Column Formwork Erected & Plumbed

Vertical timber column casing set in place against the masonry wall, checked for plumb and alignment.

Braced Column Shuttering at Fireplace

Timber column box braced with diagonal props and tied securely to resist concrete casting pressures.

Column Formwork Casing & Rebar Enclosure

Close-up view of column formwork enclosing internal steel reinforcement cages ready for pouring.

Formwork Installation at SQ Fireplace Wing

Structural carpentry crew completing the erection and anchoring of column formwork at the SQ fireplace.

Retaining Wall Water Curing at River Area

Stone retaining wall with built-in PVC weep holes undergoing water curing along the forest river boundary.

Saturating Retaining Wall Masonry Courses

Masonry joints and stone courses kept continuously damp to support cement mortar strength and durability.

Curing Columns for Retaining Wall

Water hydration applied to reinforced concrete column structures along the river forest retaining wall.

Retaining Structure Curing Inspection

Hydration curing verified across column segments and stone masonry facing near the river bank.

Ajabu Resting Contentedly Outdoors

Ajabu the Golden Retriever relaxing comfortably on the lawn following his daily outdoor exercise.

Resident Cats Reo, Mocha & Aiko Indoors

Resident cats Reo, Mocha, and Aiko gathered together peacefully indoors during feeding time.

Amani Cottage

Grounds & Lawn: Edwin

Grounds Sweeping, Litter Collection, Yucca Planting & Water Tracking

Daily property maintenance and landscaping operations at Amani Cottage on Friday, 9th October 2026 maintained pristine grounds presentation and horticultural vitality:

> ### Amani Cottage Progress Summary
>
> Edwin swept compound grounds, walkways, and entrance driveways, collecting fallen leaves and litter; planted yucca plants along garden borders; and tracked water utility consumption at 0.3 m³ for the day.

- **Grounds Sweeping & Litter Collection (Edwin):** Edwin thoroughly swept the cottage compound, clearing entrance pathways, front lawns, and paved stepping stone walkways of dry leaves, twigs, and fallen organic litter.
- **Yucca Plant Landscaping (Edwin):** New yucca plants were planted along garden margins and border beds, enriching the ornamental landscaping around the cottage grounds.
- **Utility Water Consumption Monitoring:** Water utility usage was tracked and recorded via meter inspection at 0.3 m³ consumed for daily grounds maintenance and domestic cottage needs.

📸 Photographic Field Evidence — Amani Cottage

Sequential photographic field documentation covering cottage compound sweeping, garden landscaping, and water utility monitoring:

Pristine Cottage Grounds & Swept Lawn

Broad view of Amani Cottage front lawn and stepping stone pathway cleared of fallen leaves and litter.

Swept Compound Grounds & Shed Surrounds

Lawn area and garden borders around the timber shed following sweeping and yucca planting.

Cleaned Garden Lawn & Tree Canopy

Neatly maintained cottage grounds showing swept turf beneath the mature woodland canopy.

Water Meter Consumption Reading (0.3 m³)

Close-up inspection of the Iberconta water meter recording 0.3 m³ consumed for Friday's property routines.

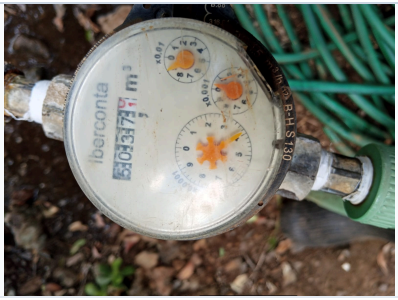

Water Utility Meter Inspection

Verification inspection of the water supply line and meter tracking daily cottage utility usage.

D **Compiled by Dennis**

Friday, 9th October 2026 • Operations Reporting
